




Schoenecker
Center

Site Plan
Received

MAR 16 2023

City of Saint Paul - DSI

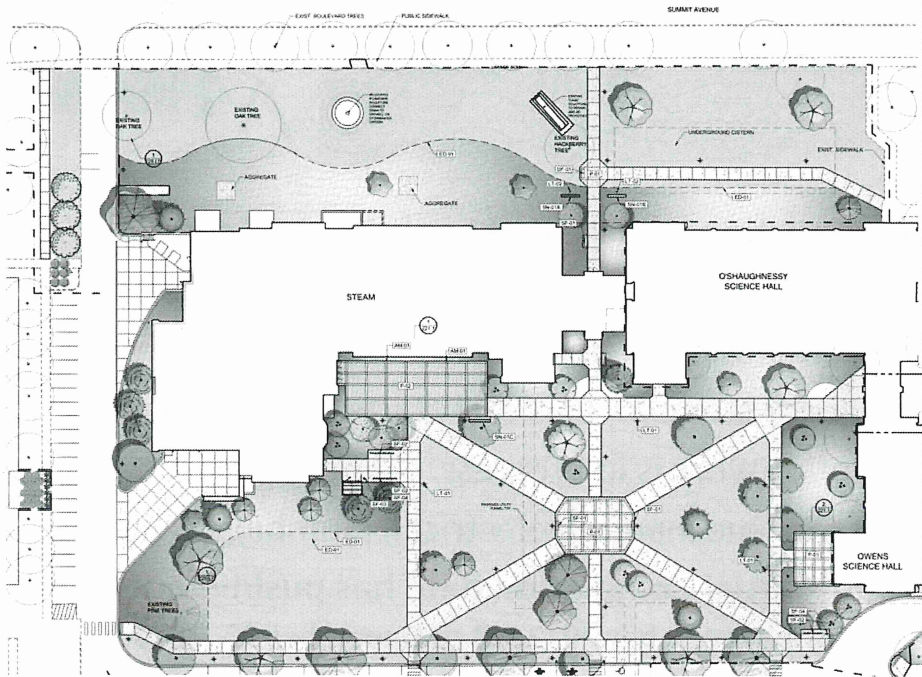

Schoenecker Center | Construction Photos



Construction Update and Look-Ahead Activities

- Steel erection & interior concrete floors are complete.
- Exterior and interior wall framing is in progress.
- Exterior stone and precast starts mid-February.
- Roofing work is in progress.
- Interior mechanical, electrical, plumbing & fire suppression in progress
- **Substantial Completion date has pushed out 30 days.**
 - From November 30, 2023 to December 29, 2023
- **Building opens Spring Semester 2024.**
