

SAINT PAUL REGIONAL WATER SERVICES

GENERAL MANAGER'S REPORT
January 11, 2024





2024 Project Details

In-House

- **545** services planned for replacement

Contracted

Hatch/Park

- Up to **411** service replacements
- Bids opened January 10, 2024
 - 2023 Contracted Price - **\$25K** / service
 - 2024 contracted price - **\$7.5K** / service

Lawson/Forest Project Area pending remaining funds


- Up to **205** service replacements



2024 Project Areas

Project areas are subject to change.

Customers will be contacted directly when plans are confirmed.

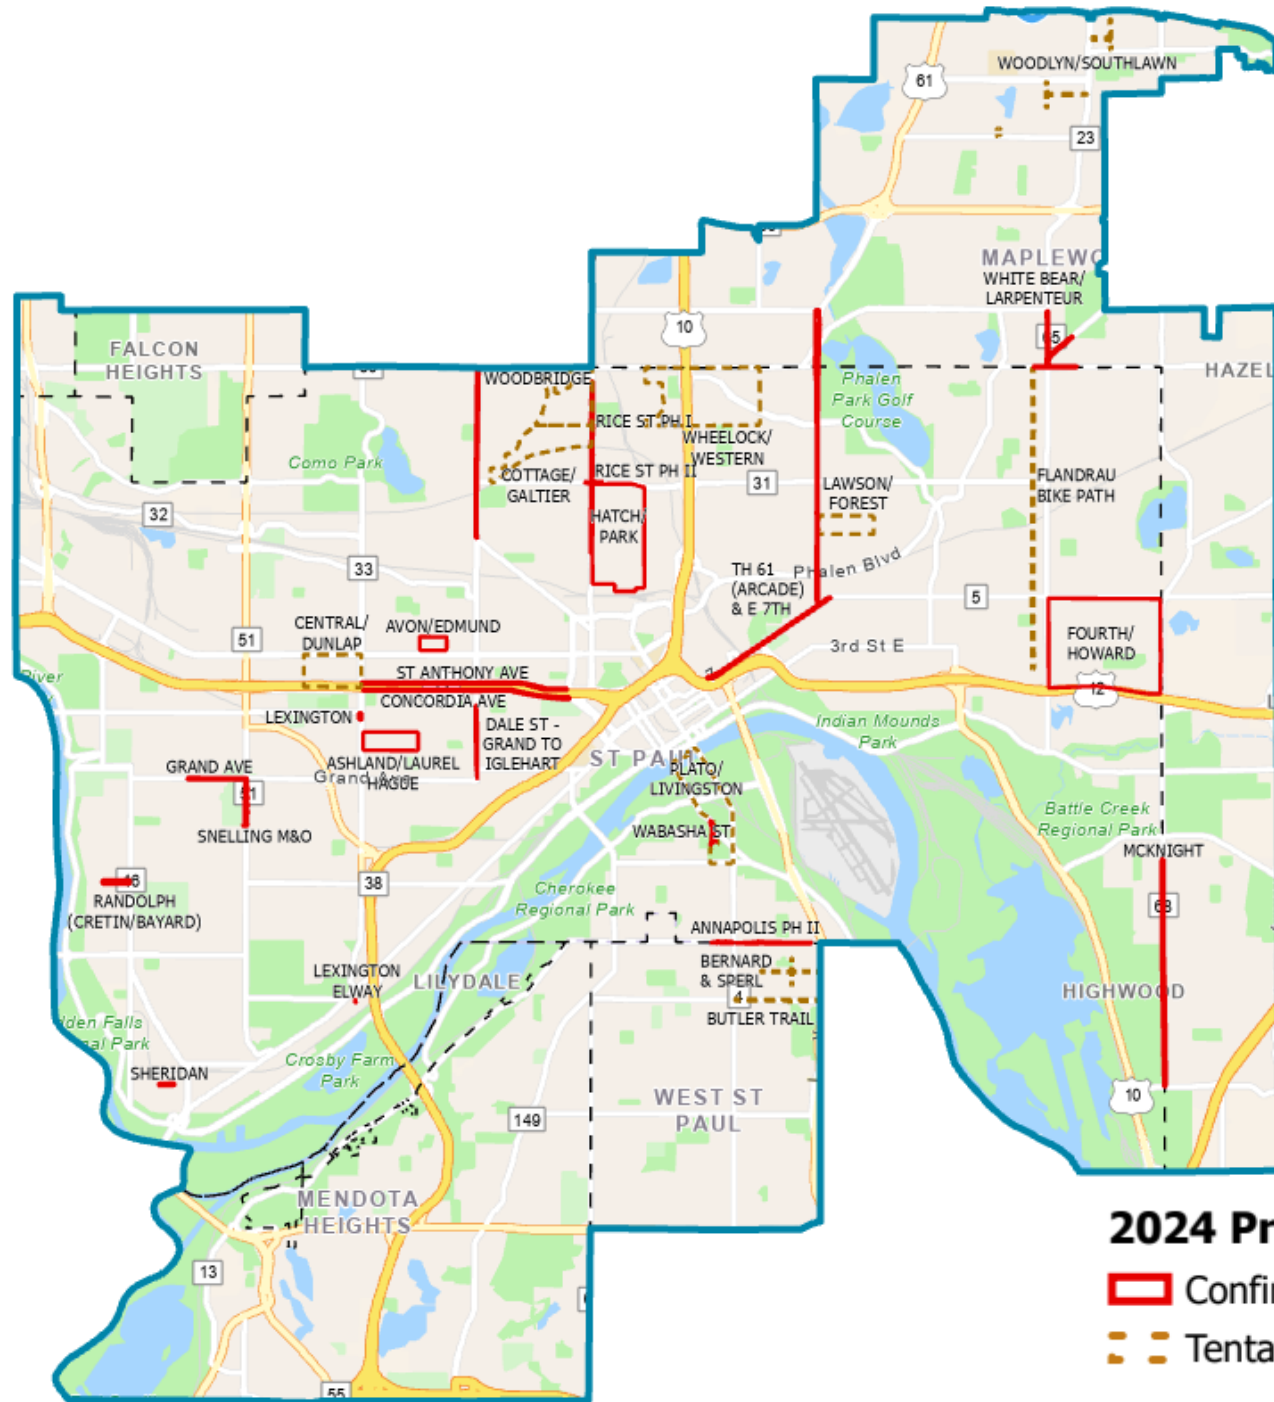


2024 Projects

- Confirmed (21)
- Tentative (10)

Corrosion Control

To reduce potential leaching, SPRWS treats the water by monitoring and adjusting pH and alkalinity levels.

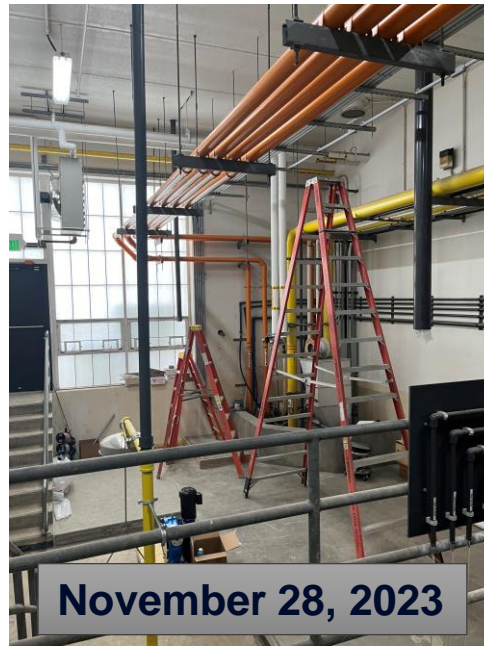

This process, called **CORROSION CONTROL**, creates a protective scale on the inside of the pipe between the water and the lead service line.

Improved corrosion control methods are being installed and will go into effect in January 2024.



December Project Updates



\$104 M Paid to Contractor
\$235 M Contracted Work

39.4 % Complete



**THANK YOU FOR YOUR
PARTNERSHIP & SUPPORT**



**SAINT PAUL REGIONAL
WATER SERVICES**

GENERAL MANAGER'S REPORT
January 11, 2024

