1629 Hartford Av Saint Paul MN
Issued 8-25-2021 Revised 9/13/21
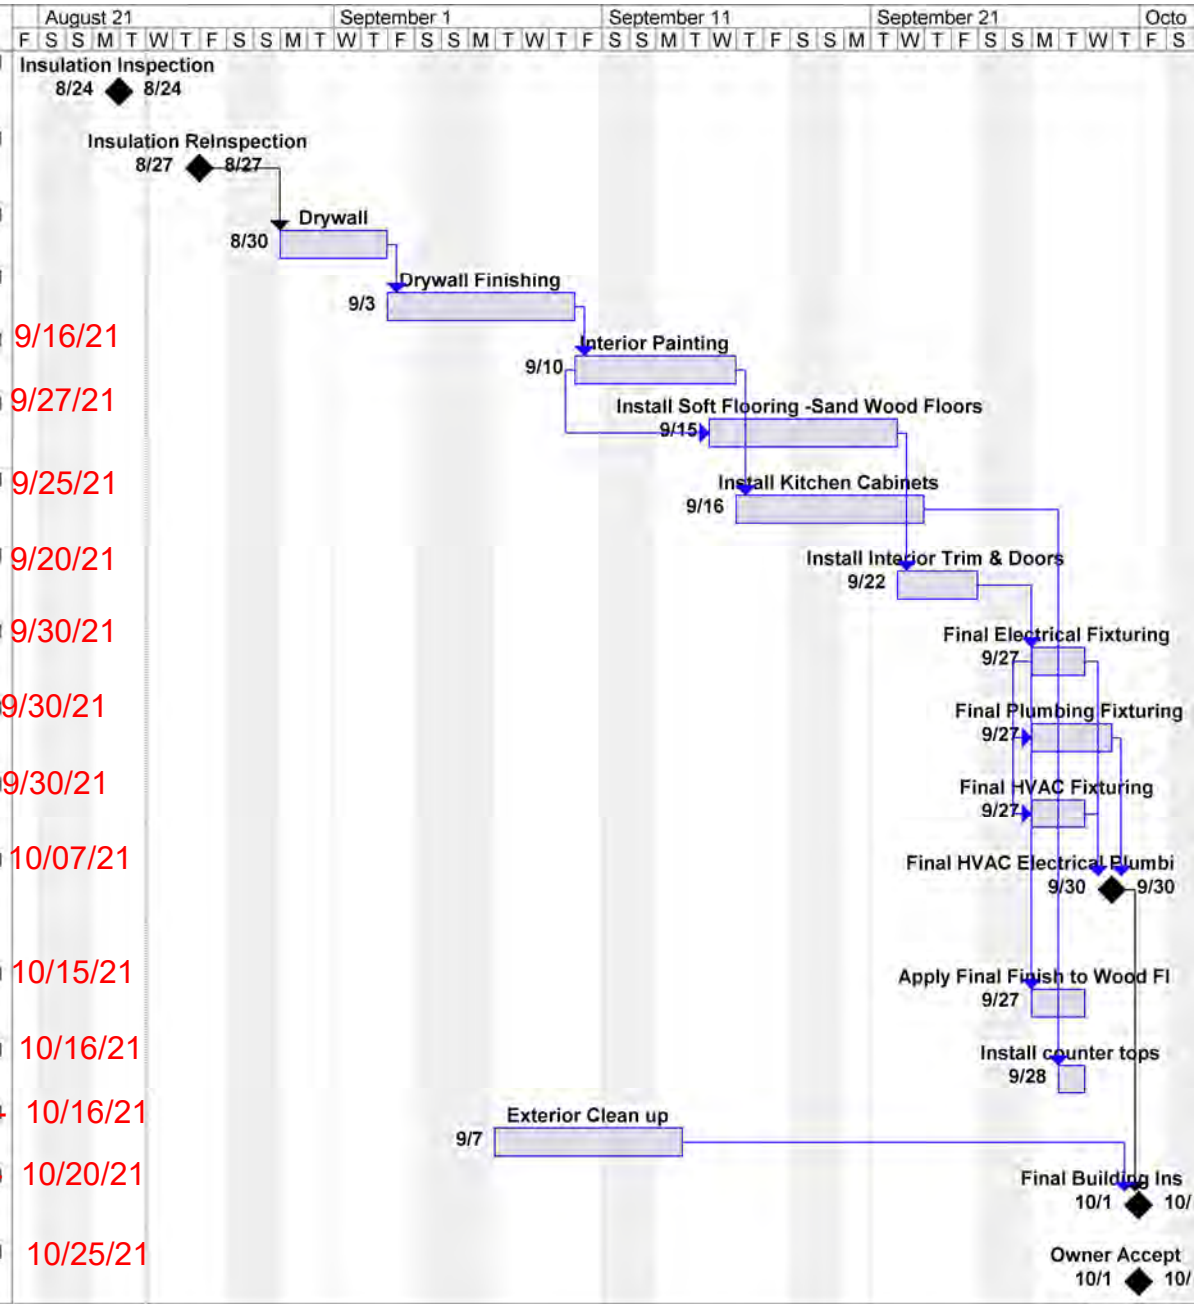
ID	Task Name	Duration	Start	
1	Insulation Inspection	1 day	Tue 8/24/21	Complete
2	Insulation Reinspection	1 day	Fri 8/27/21	Complete
3	Drywall	4 days	Mon 8/30/21	95% Complete
4	Drywall Finishing	4 days	Fri 9/3/21	40% Complete
5	Interior Painting	4 days	~~Fri 9/10/21~~	9/16/21
6	Install Soft Flooring -Sand Wood Floors	5 days	~~Wed 9/15/21~~	9/27/21
7	Install Kitchen Cabinets	5 days	~~Thu 9/16/21~~	9/25/21
8	Install Interior Trim & Doors	3 days	~~Wed 9/22/21~~	9/20/21
9	Final Electrical Fixturing	2 days	~~Mon 9/27/21~~	9/30/21
10	Final Plumbing Fixturing	3 days	~~Mon 9/27/21~~	9/30/21
11	Final HVAC Fixturing	2 days	~~Mon 9/27/21~~	9/30/21
12	Final HVAC Electrical Plumbing Inspections	1 day	~~Thu 9/30/21~~	10/07/21
13	Apply Final Finish to Wood Floors	2 days	~~Mon 9/27/21~~	10/15/21
14	Install counter tops	1 day	~~Tue 9/28/21~~	10/16/21
15	Exterior Clean up	5 days	~~Tue 9/7/21~~	10/16/21
16	Final Building Inspection	3 days	~~Fri 10/1/21~~	10/20/21
17	Owner Acceptance	1 day	~~Fri 10/1/21~~	10/25/21
