# WEIDNER APARTMENT HOMES
# RYAN COMPANIES US, INC.
# HIGHLAND BRIDGE

## Housing and Redevelopment Authority Update
## October 2025

# Agenda

1. Gateway Development (Northern HB) Update
2. Civic Square (Outlot B) Update
3. Weidner Blocks 11 & 16 Update

# Gateway Development Updates

# Gateway Updates

**Current Development Proposal:**

**Northern HB Block 1, Lot 2 Mixed Use**

- 97 Residential Units
- 23.5k Retail

**Northern HB Block 1, Lot 3 Commercial**

- 13k Retail – Tierra Encantada

# Gateway Development– Multi-family Update

- Footings and Foundations - Complete
- Structured Parking Precast and P1 Parking Slab on Grade – Complete
- 1st Floor Exterior Wall Framing – Ongoing
- 4th Floor Wood Framing – Begins 10/15
- In unit MEP Rough-in – Begins 10/27
- Roof Installation – Begins 11/5

# Gateway Development– Multi-family Update

# Gateway Development– Multi-family Update

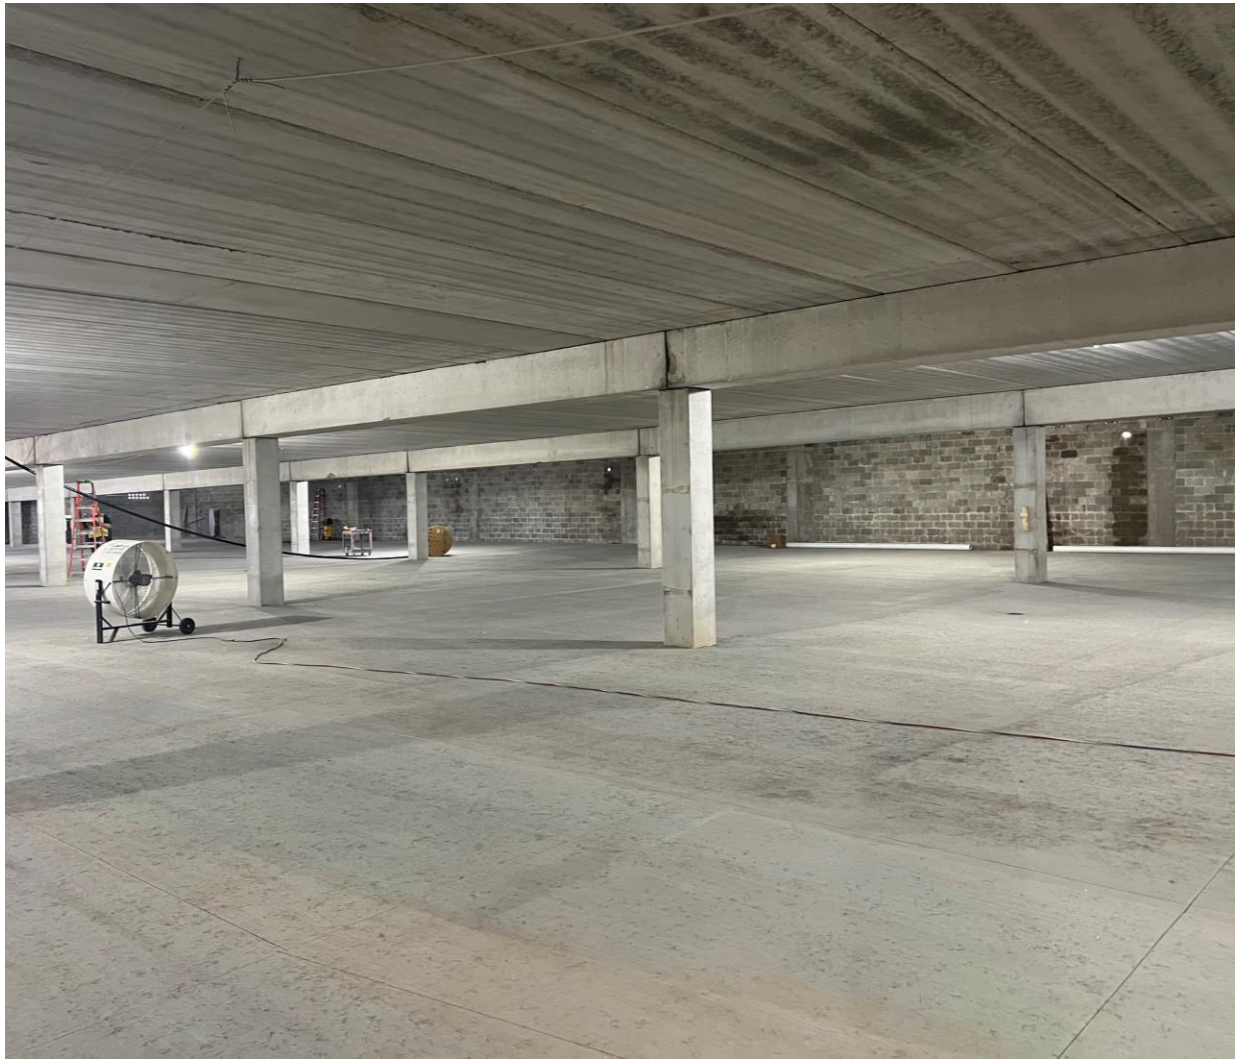

# Gateway Development– Multi-family Update

signage

CEMSTONE
Duke RENTALS

# Gateway Development – Retail Update

- Footings and Foundations Installation - Complete
- Shell Underground Plumbing & Utilities Installation - Ongoing
- Structural Steel Erection – Begins 10/27
- Roof Decking Installation – Begins 10/30
- Exterior Wall Framing – Begins 11/3
- Exterior Brick installation – Begins 11/13

# Gateway Development – Retail Update

# Gateway Development – Retail - Update

- Footings and Foundations Complete
- Utility Installation – Ongoing
- Structural Steel Erection – Ongoing
- Exterior Wall Framing – Start 10/22
- Roof Installation – Begins 10/20
- Scheduled turnover to Tierra Encantada – June 2026
- Tierra Encantada Buildout to Begin Summer 2026

# Gateway Development Updates

- Albert Kahn was the architect of the Twin Cities Assembly Plant building
- Incorporation of the “Kahn Façade” into the eastern face of the mixed-use building

# Gateway Development Updates

# Civic Square (Outlot B) Updates

# Civic Square Updates

**Current Development Proposal:**

**Civic Space**
**-Owned by Master Association along with Central Water Feature and Civic Plaza.**
**-Privately operated with public access and public easements.**

# Civic Square Updates

- Central sculptural element - reuse of the Twin Cities Assembly Plant Frieze Panels
- Bench seating, sidewalks, and landscaping extending out from central sculptural element and hardscaped square
- Outdoor dining opportunities adjacent to Gateway development
- Preservation of the angled pedestrian connection between the Civic Square and Civic Plaza

# Civic Square Updates

Preliminary Schedule (subject to change):

- End October: 60% Design Issuance
- January 2026: 90% Design Issuance
- March 2026: 100% Design Issuance
- Spring/Summer 2026: Anticipated Construction Start
- August 2026: Anticipated Construction Completion

# Civic Square Updates

# Weidner Apartment Homes

# Blocks 11 & 16

# Weidner Apartment Homes
# Blocks 11 & 16

**Block 11 (North Block)**
- +/- 170 Residential Units
- +/- 2k SF of Retail

**Block 16 (South Block)**
- +/- 180 Residential Units
- +/- 2k SF of Retail

Block 11 - Schedule

1. October 2025 - Schematic Design (SDs) and Development Design (DDs) completed
2. October 2025 - City Council Update, Neighborhood Meeting
3. November 2025 – Neighborhood Meeting, Site Plan Review Submittal (Entitlements)
4. January 2026 – Building Permit Submittal
5. April 2026 (Target) – Building Permit Issuance
    A. April 2026 – Begin Final Construction Pricing (Upon Permit Approval)
6. Spring/Summer 2026 - Construction Start

HIGHLAND Bridge

WEIDNER APARTMENT HOMES

RYAN

HIGHLAND Bridge

WEIDNER APARTMENT HOMES

RYAN

HIGHLAND Bridge

WEIDNER APARTMENT HOMES

RYAN

HIGHLAND Bridge

WEIDNER APARTMENT HOMES

RYAN

HIGHLAND Bridge

WEIDNER APARTMENT HOMES

RYAN

HIGHLAND Bridge

WEIDNER APARTMENT HOMES

RYAN

## Block 16 – Schedule

1. Currently working through site and concept design
2. Fall 2026 - Site Plan Review Submittal (Entitlements)
3. Winter 2026/2027– Building Permit Submittal
4. Spring 2027 – Building Permit Issuance
5. Spring/Summer 2027 - Construction Start

LEARN MORE AND STAY INFORMED AT
HIGHLANDBRIDGE.COM
HIGHLAND BRIDGE
SAINT PAUL
